



Arlington High School Building Project

AHS Construction Update – 6/3/20

Arlington HS Construction Schedule: April 2020 – April 2025

Construction Details


Sitework required to prepare for future construction of the new Arlington HS began in April. Work areas during this phase include the front green, the Peirce practice field and the current softball field and adjacent basketball court. Construction work hours will be Monday through Friday and follow local bylaws. Overtime and Saturday work may be required as the schedule develops. Material deliveries and other work will be coordinated around the school and traffic schedules to create as little disruption as possible.

COVID-19 Update

The health and safety of the community and workers on-site are of the highest priority and were taken into consideration in all project-related decisions. Per Governor Baker's announcement, construction work is deemed 'essential' and can continue. For the school to be completed on time, it is very important to maintain the original construction timeline as closely as possible. The construction team will also be maximizing the schedule as students are off-site during this time. The Town of Arlington continues to monitor all state and federal guidelines regarding best practices during this unusual time and will modify recommendations as necessary to maintain safety and health for our community and construction workers.



PHASE 1 SITEWORK (May 2020 – June 2020)

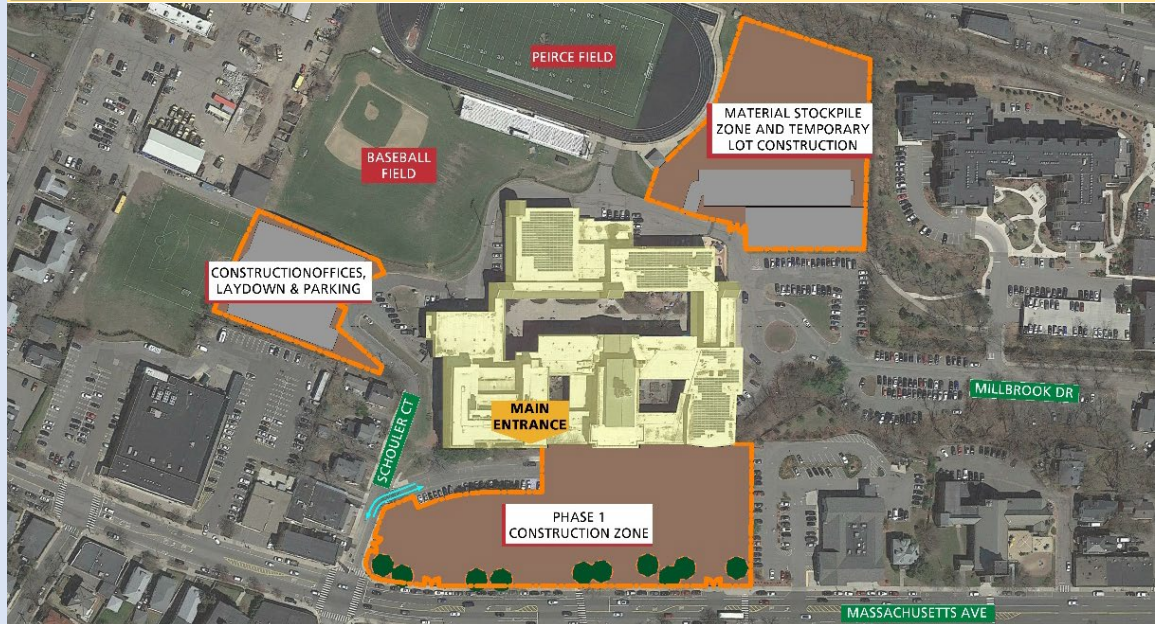

Construction Look Ahead – Week of June 8, 2020

The above diagram covers all work to be performed during the current phase. Specific work to be performed this week includes:

Public Way Impacts

- Mass Ave entrance and circular drive closed
- District offices will be accessible via Schouler Court and parking in front of Fusco Building

Interior Site Activities

- Renovation of classroom spaces for temporary phasing

General Site Activities

- Schouler Court:
 - Water tie-in
- Mass Ave Front Lawn:
 - Removal of top-soil and pavement
 - Installation of drainage line
- West Parking Lot:
 - Paving
- Current Basketball Court/Softball Field/Pre-School Playground:
 - Paving
 - Demo of playground

Weekend Work

- None at this time

Sign up for Weekly Construction Updates <https://ahsbuilding.org/news/construction-updates/>

For more information, visit: www.ahsbuilding.org

Email questions or concerns to: ahsbuilding@arlington.k12.ma.us

**For immediate, on-site assistance contact Hal Raymond,
Skanska Site Representative, (617) 352-8593**



CONSIGLI
Est. 1905

ARLINGTON HIGH SCHOOL

WEEKLY UPDATE – WEEK OF JUNE 08, 2020

Progress Photographs – Taken 06/01/2020



Photograph 1: Mass Ave Front Lawn - Sitework



Photograph 2: Mass Ave Front Lawn – Pipe Delivery



Photograph 3: Mass Ave Front Lawn – Dust Control



Photograph 4: West Parking Lot Prepped and Ready for Paving



Photograph 5: Current softball field/Future Contractor lay down area– Bulldozer Preparing for Paving



Photograph 6: Playground with Temp. Fence Ready for Demolition
